

Eduvos Assessment Coversheet

Academic Details

Campus: **MOWBRAY**

Faculty: **INFORMATION TECHNOLOGY (DATA SCIENCE)**

Module Code: **ITPMA2-33**

Lecturer's Name: **MR. ANDREW DAVIES**

Group (if applicable) **1**

Assessment Details

Assessment Type: **FORMATIVE ASSESSMENT**

Assignment/Brief Number: **ITPMA2-33 PROJECT**

Due Date/ Submission Date: **28th August 2026**

Student Details (Group, if applicable)

#	Full Name	Student Number	Contact Number	% Participation	Signature
1					
2					
3					
4					
5					
6					

Student Details (Individual, if applicable)

Student Full Name: OLATUNJI OLAYINKA OLUWASEUN

Student Number: EDUV8024667

Academic Integrity

AI Disclosure Completed



Yes




No

Declaration:

I declare that this assessment is my own original work except for source material explicitly acknowledged. I confirm that this work has not previously been submitted for assessments in any course. I acknowledge the institutional AI policy and confirm that AI tools have only been used as stipulated and documented in the AI Disclosure Appendix.

Student Signature



Date

27th August 2026

Lecturer Use Only

Lecturer Comments:

Marks Awarded (%):

Lecturer Signature:

Date:

Table of Contents

Eduvos Assessment Coversheet.....	1
Question 1.1:	4
Question 1.2:	5
Question 1.3:	7
Question 1.4:	8
Question 1.5:	9
Question 1.6:	11
Question 1.7:	12
Table of Figures.....	14
AI Disclosure Appendix.....	16
Declaration:	16

Question 1.1:

Effect of lack of stakeholder ownership and project governance

It was observed that the company under study was plagued with overwhelming workload, schedule overruns measured in years and frequent project restarts, coupled with integration challenges. Up until the point where PM Solutions was commissioned to step in and intervene, the organization did not clearly identify stakeholders or correctly ascribe project ownership, consequently, numerous re-initiations of business requirements occurred, translating to very little progress over a long period of time (PM Solutions, 2026).

In correlation with PM several documentations, having high stakeholder and user involvement critically contribute to project success. Likewise low stakeholder engagement happens to be a leading factor that contributes to project failure (PM Essentials, 2017).

It is observed from echoes of the Standish Group's CHAOS Report and the PMI's Pulse of the Profession Survey that projects which had high stakeholder support were more likely to succeed than projects with low stakeholder support fundamentally because when there is higher stakeholder involvement, requirements are clear because expectations are well defined, but on the contrary, project goals and scope are found to be fuzzy and fluid for projects with low stakeholder involvement (PM Essentials, 2017). Concerning the organization under observation, this fluidity is clearly illustrated by multiple restarts, technologies discarded several years of schedule overrun (PM Solutions, 2026). Project governance is the system of roles, decision rights, oversight process and accountability structures which reign to make sure that projects align with the goals of the business all through the delivery process and its absence in this particular organization's scenario made things really go bad (Rocketlane, 2026). This resulted in a situation where there is literally no means for compelling the making of critical decisions required for project progress which manifested as high staff and technologies turnover giving rise to numerous restarts and integration challenges such that even basic requirements could not be met successfully (PM Solutions, 2026). This actually aligns with governance documentation that suggests that organizations without proper governance framework will have challenges such as misalignment with organizational goals, lack of stakeholder buy-in, poor communication channels, scope creep and change management gaps, and insufficient resource allocation (Galorath, 2025). In the organization's scenario, the absence of the governance framework meant the project team was stranded anytime there was need for escalation of issues based on the fact that what was in place was some operational maintenance structure which caused an overwhelming workload to persist instead of being sorted (PM Solutions, 2026).

Impact of stakeholder management and project governance on project success

Ultimately, we can say that the lack of stakeholder ownership and governance in this particular scenario is evidently consequentially observable in repeated restarts, years of schedule overrun,

discarded work and project deliverables close to nothing but wireframes before PM Solutions stepped into the situation, thereby reflecting a model case of inefficiency, delays, increased costs and failure to meet project objectives (Galorath, 2025).

Question 1.2:

I would dispense my role as assigned program manager at the beginning of the crisis along these areas:

Project review and recovery assessment: Initial move would be to pause the ongoing development and attempt to employ structured recovery assessment in accordance with troubled-project recovery models: intervention, assessment, and determining the root cause of poor performance, planning, implementation, control, and closure (PMI, 2000) and (PMI, 2007). The fact that PM Solution's consultant commenced by doing a full project review before getting to any fresh work buttresses my decision (PM Solutions, 2026). On engaging this project review and recovery assessment stage, the result should produce a project state report that candidly reveals the true state of the project to the stakeholders with the intention of recalibrate expectations while providing concrete basis for making sound decisions going forward (PMI, 2000).

Requirements Management: The very thought that "even basic business requirements" kept being re-initiated on and on shows that there was fundamentally, no proper identification of requirements from the word go (PM Solutions, 2026). To rectify this, I would apply these standard requirements management processes: planning, gathering and analysis, verification and change management (Smartsheet, 2022) - while ensuring that every requirement is prioritized and signed-off by identified stakeholders prior to any project team members doing their part (Stell Engineering, 2025). This is mirrored in the scenario being considered by, "early management review of requirements and prior authorizations before work is assigned" (PM Solutions, 2026), which definitely emphasizes change control process.

Agile/Scrum Implementation: Instead of doing any elaborate replanning, I would employ quick restarts with several controlled sprints in order to progressively provide proof-of-concept just as PM Solutions approached the issue (PM Solutions, 2026). For a small team without any sophisticated means, Scrum's underlying principles transparency, inspection and adaptation (Tuleap, 2026), can help achieve provable milestones and checkpoints for detecting challenges early instead of just finding out after years of sinking resources and labor as was the case before. Prioritization happens in an incremental and iterative fashion during sprints instead of only at some problematic starting point (Tuleap, 2026).

JIRA and Workflow Management: JIRA was already being used in the organization; hence, this means therefore that the quickest means of recovery was enhancing its use instead of launching the

use of new tools (PM Solutions, 2026). In a similar way, I would customize agile workflows and boards for backlogs and sprint boards, do tracking with status columns and burndown charts, ensure reporting by making dashboards accessible to stakeholders, and workflow automation (Atlassian, 2026). Making business analysts and QA work closely with developers as exemplified in this scenario with PM solutions eradicates the shortfall between written requirements and actually understood requirements, which highlights the major issue causing re-initiation and rework from the word go (PM Solutions, 2026).

Kanban and WIP Limits: The Kanban board is used by agile teams to make work visible across the project pipeline and reveal points at which the work is piling up or issues are lingering (Atlassian, 2026). In order to orchestrate a scenario where team members don't get new work items started before existing work items get finished, I would employ work-in-progress (WIP) limits for every column just as it was applied in the scenario under consideration thereby enhancing task yield and avoid the team being overwhelmed with work-in-progress items (PM Solutions, 2026). This gives an outcome such that, even though all team members are predominantly busy, it becomes a manageable problem since WIP limits helps ensure that team members that ever get free to work on the project know exactly where to focus in order to move the work forward.

Resource Management: It was identified that project personnel experienced serious challenges due to turnover of staff and technologies causing the reported failure (PM Solutions, 2026). What I would do to resolve these challenges is to employ cross-training and encourage proper handover practices to ensure that no team member is no single point of failure, ensure resource redundancy or backup for critical skills, and ensure team members are not overworked by balancing workload across operational responsibilities and new developmental work – this blend adequately reduces turnover due to burnout and associated schedule risk (Productive, 2025).

Justification of Techniques: These techniques don't get used as siloed contraptions, but they intricately interplay to bolster each other. Accountability is entrenched via governance and continuous review; requirements and change management eradicate the requirement re-initialization loop if it can not get fixed with governance; a safe and continuous rebuild impetus is achieved with Agile/Scrum; JIRA helps to visibly organize the project work components to be easily accessible by team members; Kanban and WIP limits then translate this visibility into trackable output; and resource management helps to prevent the accrued wins from being lost or cancelled like was the case in the original collapse. A concurrent application of these techniques is in line with the observable result which PM Solutions recorded: task throughput was enhanced exponentially and rejection rates by QA declined to 5% from about 30% in a 6-month period (PM Solutions, 2026).

Question 1.3:

The WBS is a very important tool in project management fundamentally because it provides the basis for deciding how to actually execute the tasks that have been highlighted (Schwalbe, 2019). With guidance from the ERP system implementation steps, the level 3 WBS is created by breaking them down as follows: Level 0 – the project itself, Level 1 – phases, Level 2 – the eight tasks as given in the brief, and Level 3 – sub-deliverables under each of the given tasks. And once created, this WBS can be used to monitor the project scope because every piece of work is traceable back to one of the eight tasks given in the scenario.

Level	WBS Element	Description	Predecessor	Duration
Level 0	1.0 ERP System Implementation Project	Overall Project Level		
Level 1	1.1 Initiation and Planning	First Phase		
Level 2	1.1.1 Planning and Discovery (Task 1)	Research, choose system, form the project team, and define requirements	None	5 days
Level 3	1.1.1.1 Research candidate ERP systems			
Level 3	1.1.1.2 Select ERP system and vendor			
Level 3	1.1.1.3 Set up the project team and define requirements			
Level 1	1.2 Design and Development	Second Phase		
Level 2	1.2.1 Design (Task 2)	Create detailed design from requirements	Task 1	4 days
Level 3	1.2.1.1 Map existing procedures			
Level 3	1.2.1.2 Draft detailed system design			
Level 3	1.2.2 Software Development (Task 3)	Build ERP architecture, test and troubleshoot software	Task 2	3 days
Level 3	1.2.2.1 Build the ERP architecture			
Level 3	1.2.2.2 Test and troubleshoot the software			
Level 1	1.3 Data and Configuration	Third Phase		
Level 2	1.3.1 Data preparation and Migration (Task 4)	Prepare and migrate data	Task 2 and Task 3	4 days
Level 3	1.3.1.1 Clean and prepare data			
Level 3	1.3.1.2 Migrate data to new system			
Level 2	1.3.2 System Configuration	Configure the ERP	Task 4	6 days

	(Task 5)	to client needs		
Level 3	1.3.2.1 Configure modules and workflows			
Level 3	1.3.2.2 Set user roles and permissions			
Level 1	1.4 Deployment and Testing	Fourth Phase		
Level 2	1.4.1 System Deployment (Task 6)	Install system, integrate it with client hardware / software	Task 5	5 days
Level 3	1.4.1.1 Install the system on client hardware			
Level 3	1.4.1.2 Integrate with existing systems			
Level 2	1.4.2 Software Testing (Task 7)	Test system before and after going live	Task 5 and Task 6	4 days
Level 3	1.4.2.1 Execute testing before going live			
Level 3	1.4.2.2 Execute testing after going live			
Level 1	1.5 Training and Closure	Fifth Phase		
Level 2	1.5.1 Employee Training (Task 8)	Train the workforce on how to use the ERP system	Task 7	4 days
Level 3	1.5.1.1 Prepare training materials			
Level 3	1.5.1.2 Deliver the training sessions			

Table 1 - Level 3 WBS based on the guidance of the ERP system implementation steps.

Question 1.4:

Here below is the diagram for the eight ERP tasks as nodes on an AON network Diagram as specified in the scenario. Each node has an Early Start (ES), Task ID, and Early Finish (EF) at the top row of each task element, and Late Start (LS), Duration and Late Finish (LF) at the bottom row of each task element, and Float with the Task Name in the middle. Task 4 (Data Preparation & Migration) as specified, depends on both Task 2 & 3, and Task 7 (Software Testing) depends on both Task 5 & 6, but these extra lines are depicted with dashed lines because they do not change the critical path since Task 3 already depends on Task 2, and Task 6 already depends on task 5.

Activity-on-Node (AON) Network Diagram

LEGEND

ES	Task ID	EF
Float	Task Name	
LS	Duration	LF

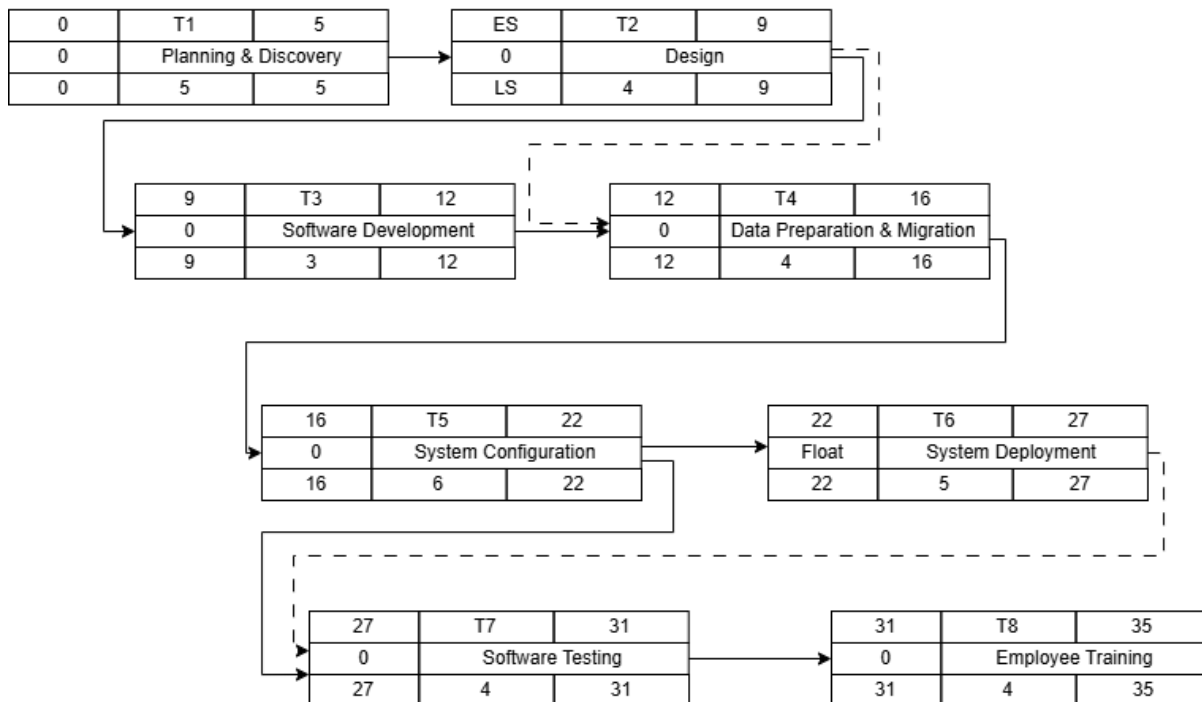


Figure 1 - Activity-on-Node (AON) Network Diagram

The Project length = 35

Question 1.5:

Calculations:

In order to calculate the critical path, using the forward pass (Early Start/Early Finish) and the backward pass (Late Start/Late Finish), the total float for each task resolves to zero as shown in the table below, because Task 3 already depends on Task 2 (so the Task 2 requirement for Task 4 is automatically satisfied later), the Task 6 already depends on Task 5 (so the Task 5 requirement for Task 7 is automatically satisfied later). This means that the network behaves as if it were a straight chain of eight tasks strung together.

Task	Duration	ES	EF	LS	LF	Total Float	Critical?
T1 Planning & Discovery	5	0	5	0	5	0	Yes
T2 Design	4	5	9	5	9	0	Yes
T3 Software Development	3	9	12	9	12	0	Yes
T4 Data Preparation & Migration	4	12	16	12	16	0	Yes
T5 System Configuration	6	16	22	16	22	0	Yes
T6 System Deployment	5	22	27	22	27	0	Yes
T7 Software Testing	4	27	31	27	31	0	Yes
T8 Employee Training	4	31	35	31	35	0	Yes

Table 2 - Calculation of critical path

The Critical path is: T1 → T2 → T3 → T4 → T5 → T6 → T7 → T8, and the duration of the project is 35 working days with zero float in every task.

Discussion:

It is observed that all the tasks in the project are situated on the critical path, hence any delay to any individual task will cause delay to the entire ERP delivery date, making it immensely important for a critical path analysis to keep the project from derailing. To start with, critical path analysis helps the project manager know exactly which tasks need to be closely monitored in order to best allocate resources, since there is no free time available to buffer any delays. Then, it also serves as an early warning system because if any task overshoots its planned completion date by even one day, the project manager knows the project completion date definitely has to move and can decisively act to accommodate the change.

Critical path analysis can also support better decision making when problems come up. If a delay happens, the project manager can use the network diagram to test "what-if" options, such as accelerating a task by throwing in more resources to shorten duration or fast-tracking two tasks to run partly in parallel. It also helps with communication: because every task is critical, the project manager can tell the whole team and stakeholders clearly that no task is low priority, which supports the kind of transparency and stakeholder engagement discussed in sections 1.1 and 1.2. Ultimately, tracking progress against the critical path regularly lets the project manager update forecasts and keep stakeholders informed, which is one of the key lessons from the original case study, where not having good sight of project progress was one of the root problems before PM Solutions became involved.

Question 1.6:


Provided below is the table that highlights the task dependencies precisely as inputted into Project Libre, along with the Gantt chart produced thereafter. All eight tasks are depicted on the chart as critical (red bars), given that the critical path as calculated earlier spans the entire project.

Task Dependency Table

Task ID	Task Name	Duration (days)	Predecessor(s)	Start (day)	Finish (day)
T1	Planning and Discovery	5	None	0	5
T2	Design	4	T1	5	9
T3	Software Development	3	T2	9	12
T4	Data preparation and migration	4	T2, T3	12	16
T5	System configuration	6	T4	16	22
T6	System deployment	5	T5	22	27
T7	Software testing	4	T5, T6	27	31
T8	Employee training	4	T7	31	35

Table 3 - Task Dependency Table for the ERP Implementation Project

And this is the snapshot of the data inputted into Project Libre.

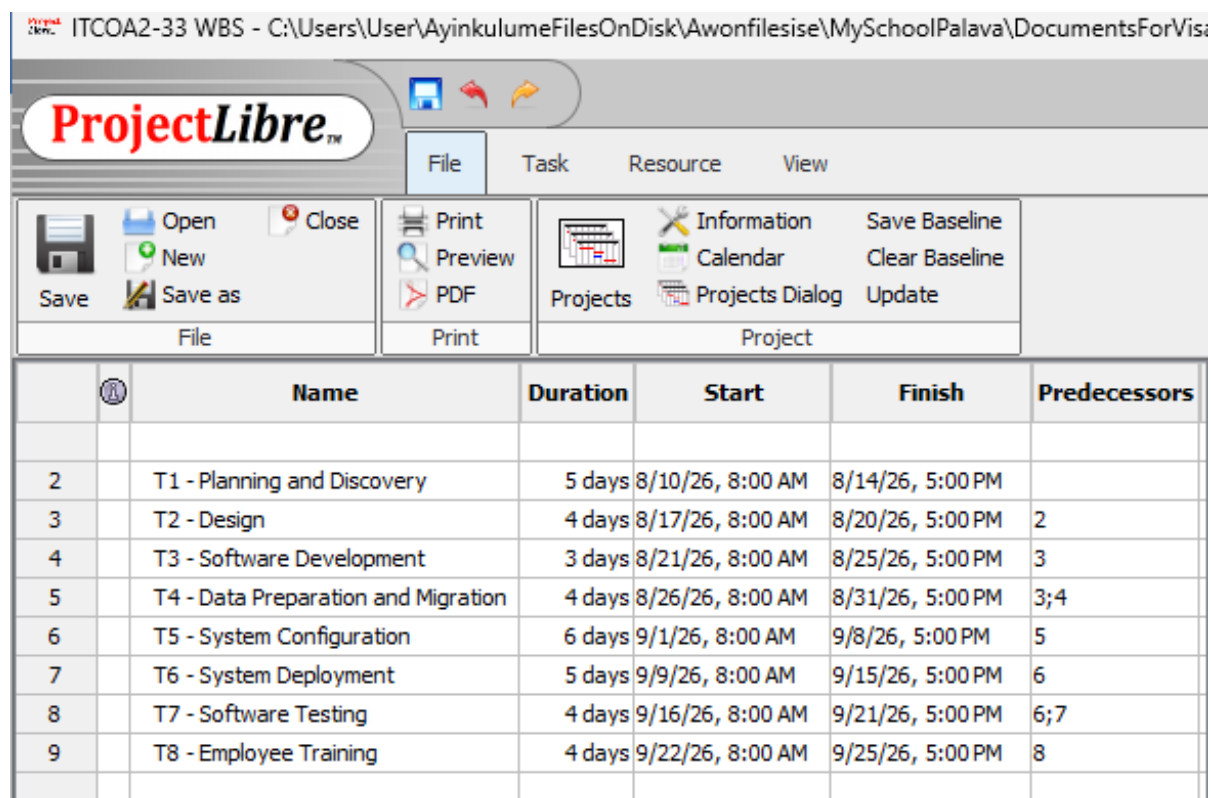


The screenshot shows the Project Libre application window. The title bar reads "ITCOA2-33 WBS - C:\Users\User\AyinkulumeFilesOnDisk\Awonfilesise\MySchoolPalava\DocumentsForVisi". The menu bar includes "File", "Task", "Resource", and "View". The toolbar contains icons for "Save", "Open", "Close", "New", "Save as", "Print", "Preview", "PDF", "Projects", "Information", "Calendar", "Projects Dialog", "Save Baseline", "Clear Baseline", and "Update". Below the toolbar is a table with the following data:

ID	Name	Duration	Start	Finish	Predecessors
2	T1 - Planning and Discovery	5 days	8/10/26, 8:00 AM	8/14/26, 5:00 PM	
3	T2 - Design	4 days	8/17/26, 8:00 AM	8/20/26, 5:00 PM	2
4	T3 - Software Development	3 days	8/21/26, 8:00 AM	8/25/26, 5:00 PM	3
5	T4 - Data Preparation and Migration	4 days	8/26/26, 8:00 AM	8/31/26, 5:00 PM	3;4
6	T5 - System Configuration	6 days	9/1/26, 8:00 AM	9/8/26, 5:00 PM	5
7	T6 - System Deployment	5 days	9/9/26, 8:00 AM	9/15/26, 5:00 PM	6
8	T7 - Software Testing	4 days	9/16/26, 8:00 AM	9/21/26, 5:00 PM	6;7
9	T8 - Employee Training	4 days	9/22/26, 8:00 AM	9/25/26, 5:00 PM	8

Screenshot 1 - The Task Dependency table data inputted into Project Libre

The Gantt Chart

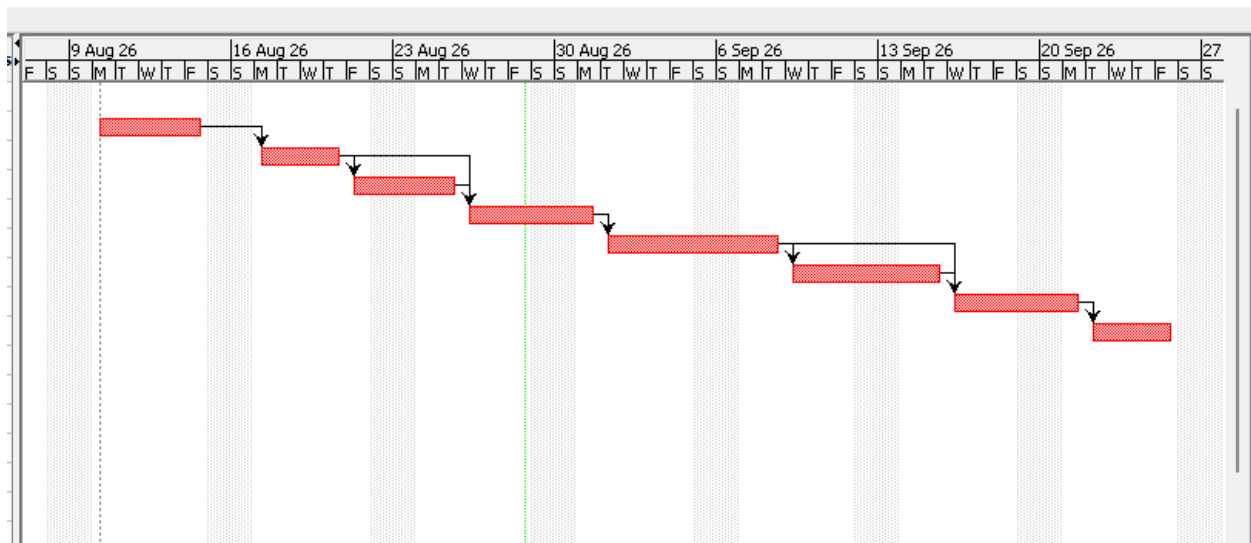

Screenshot 2 - Gantt Chart - ERP System Implementation Project

Question 1.7:

First Limitation:

The Gantt chart works well at showing when a task starts and ends, but in large project with interlinked tasks situations, it becomes difficult to clearly see why a task is scheduled at that time or which other tasks it depends on, thereby making it hard to see the ripple effect of delays in tasks through the schedule.

Tools which juxtapose dependencies and timelines highlight that critical path activities require special attention since delays in those activities have repercussion throughout the overall project (Productive, 2025), which can be easily missed with the use of a plain Gantt chart. This limitation is even noticed more in a complex project like this ERP implementation, where Task 4 depends on two earlier tasks and Task 7 depends on two earlier tasks, but the Gantt chart alone does not show this clearly. This can be overcome by pairing the Gantt chart with a network diagram just like the one in question 1.4 in order for the team to see both the timeline and the way the different tasks depend on each other.

Second Limitation:

The fundamental assumption upon which the Gantt chart operates is that people and equipment are available whenever the schedule needs them, without making provision for double-booking of staff across tasks, or if a specialist's skill could be a bottleneck on the project, making Gantt charts less effective for projects with shared or limited resources as is the case with this project where the same team could be required for both configuration and testing at the same time. To overcome this limitation, resource levelling and capacity planning can be employed along with the Gantt chart so that workloads are evaluated and rebalanced before the plan is finalized (Productive, 2025). Using

the Gantt chart together with the Kanban board and WIP limits as mentioned earlier in question 1.2 also helps expose when a team is overloaded, which cannot be achieved by a Gantt chart alone.

Table of Figures

Figure 1 - Activity-on-Node (AON) Network Diagram	9
Table 1 - Level 3 WBS based on the guidance of the ERP system implementation steps.	8
Table 2 - Calculation of critical path.....	10
Table 3 - Task Dependency Table for the ERP Implementation Project.....	11
Screenshot 1 - The Task Dependency table data inputted into ProjectLibre	11
Screenshot 2 - Gantt Chart - ERP System Implementation Project.....	12

References

- Atlassian. (2026). *Putting the 'flow' back in workflow with WIP limits*. Retrieved August 18, 2026, from <https://www.atlassian.com/agile/kanban/wip-limits>
- Galorath. (2025). *Project Governance: Definition, Components, Structure & Models*. Retrieved August 17, 2026, from <https://galorath.com/project/governance/>
- PM Essentials. (2017). *Stakeholder Management: A Key to Project Success*. Retrieved August 17, 2026, from <https://pmessentials.us/stakeholder-management-key-project-success/>
- PM Solutions. (2026). *PM Governance Combined with Agile Tools Improves Delivery and Quality of Financial Services Programs*. Retrieved August 17, 2026, from <https://www.pmsolutions.com/case-studies/pm-governance-combined-with-agile-tools-improves-delivery-and-quality-of-fi>
- PMI. (2000). *Six steps to project recovery*. Retrieved August 18, 2026, from <https://www.pmi.org/learning/library/six-steps-project-recovery-4641>
- PMI. (2007). *Five critical first steps in recovering troubled projects*. Retrieved August 18, 2026, from <https://www.pmi.org/learning/library/critical-steps-recovering-troubled-projects-7352>
- Productive. (2025). *What Is Resource Allocation In Project Management?* Retrieved August 18, 2026, from <https://productive.io/blog/resource-allocation-in-project-management/>
- Rocketlane. (2026). *What is Project Governance? A Complete Guide to Frameworks, Components, and Best Practices in 2026*. Retrieved August 17, 2026, from <https://www.rocketlane.com/blogs/what-is-project-governance>
- Schwalbe, K. (2019). *Information Technology Project Management* (9 ed.). Boston, USA: Cengage.
- Smartsheet. (2022). *Requirements Management 101: Processes, Plans, and Best Practices*. Retrieved August 18, 2026, from <https://www.smartsheet.com/content/requirements-management>
- Stell Engineering. (2025). *How to Create a Requirements Management Plan*. Retrieved August 18, 2026, from <https://stell-engineering.com/blog/requirements-management-plan>
- Tuleap. (2026). *Understanding Agile Scrum in 10 minutes*. Retrieved August 18, 2026, from <https://www.tuleap.com/agile-scrum-in-10-minutes/>

AI Disclosure Appendix

AI tool used	Purpose / how it was used	How I verified or adapted the output
N/A – Used normal Google Searching	Searched Google to gain general, introductory understanding to be able to ponder on what needs to be assessed.	Did deep introspection on the content of authoritative and peer-reviewed sources in relation to what is to be assessed then applied the understanding gained to the focus of the assessment.

Declaration:

I/we declare that this assessment is my/our own original work, except for source material explicitly acknowledged. I/we confirm that any use of Artificial Intelligence (AI) tools has been applied only as permitted by the assessment instructions and has been fully disclosed where required.

I/we understand that I/we remain responsible for the accuracy, originality, and academic quality of this submission. I/we am/are aware of the institution's policies on academic integrity and the requirements relating to the responsible use of AI in assessments.

I/we acknowledge that failure to comply with these requirements, including undeclared or inappropriate AI use, may result in academic penalties or disciplinary procedures in accordance with institutional policy.

Student Signature(s)	Date
	27th August 2026
